ATTACHMENT 5: June 2011 Revised WSIP - Project-Level Schedules

Project Name	Start	Finish
Regional Improvement Projects	31-Mar-00 A	29-Jul-16
San Joaquin Region	01-Jul-02 A	25-Mar-14
CUW36401 Lawrence Livermore Water Quality Impro	02-Feb-04 A	14-Sep-11
CUW37301 San Joaquin Pipeline System	19-Aug-02 A	25-Mar-14
CUW37302 Rehabilitation of Existing San Joaquin Pip	03-Jul-06 A	12-Mar-14
CUW38401 Tesla Treatment Facility	01-Jul-02 A	28-Sep-12
Sunol Valley Region	19-Dec-01 A	29-Jul-16
CUW35201 Upper Alameda Creek Filter Gallery	30-Sep-03 A	15-Jul-16
CUW35501 Standby Power Facilities - Various Locatio	11-Jul-02 A	22-Dec-10 A
CUW35901 New Irvington Tunnel	19-Dec-01 A	31-Oct-14
CUW35902 Alameda Siphon #4	19-Dec-01	12-Jun-12
CUW37001 Pipeline Repair & Readiness Improvement	21-Apr-03 A	16-Apr-09 A
CUW37401 Calaveras Dam Replacement	03-Sep-02 A	29-Jul-16
CUW37402 Calaveras Reservoir Upgrades (Completed)	19-Nov-03 A	28-Jul-06 A
CUW37403 San Antonio Backup Pipeline	17-Dec-03 A	09-Mar-15
CUW38101 SVWTP Expansion & Treated Water Rese	22-Apr-05 A	05-Dec-13
CUW38601 San Antonio Pump Station Upgrade	01-Jul-04 A	07-Dec-11
Bay Division Region	19-Dec-01 A	13-Nov-15
CUW35301 BDPL Nos. 3 & 4 Crossover/Isolation Val	06-Jan-03 A	31-Jul-09 A
CUW35302 Seismic Upgrade of BDPL Nos. 3 & 4	22-Oct-04 A	26-Apr-15
CUW36301 SCADA System - Phase II	22-Apr-05 A	24-Feb-12
CUW36801 BDPL Reliability Upgrade - Tunnel	19-Dec-01 A	13-Nov-15
CUW36802 BDPL Reliability Upgrade - Pipeline	19-Dec-01 A	05-Mar-13
CUW36803 BDPL Reliability Upgrade - Relocation of	24-Apr-06 A	28-May-10 A
CUW38001 BDPL Nos. 3 & 4 Crossovers	17-Feb-04 A	17-May-13
CUW38901 SFPUC/EBMUD Intertie	24-Jun-02 A	30-Dec-11
CUW39301 BDPL No. 4 Condition Assessment PCCP	04-Aug-06 A	06-Feb-09 A
Peninsula Region	01-Nov-00 A	06-Jul-16
CUW35401 Lower Crystal Springs Dam Improvements	01-Nov-00 A	27-Sep-12
CUW35601 New Crystal Springs Bypass Tunnel	07-Jan-02 A	29-Mar-12
CUW35701 Adit Leak Repair - Crystal Springs/Calave	01-Apr-05 A	31-Jul-08 A
CUW36101 Pulgas Balancing - Inlet/Outlet Work (Com	15-May-02 A	11-May-06 A
CUW36102 Pulgas Balancing - Discharge Channel Mo	01-Apr-05 A	30-Jul-10 A
CUW36103 Pulgas Balancing - Structural Rehabilitatio	03-Apr-06 A	24-Feb-12
CUW36105 Pulgas Balancing - Modifications of the Ex	02-Apr-07 A	30-May-12
CUW36501 Cross Connection Controls (Completed)	01-Jul-03 A	30-Apr-09 A
CUW36601 HTWTP Short-Term Improvements (Dem	04-Sep-02 A	14-Nov-06 A
CUW36603 HTWTP Short-Term Improvements - Coag	03-Jul-06 A	28-Jul-10 A
CUW36701 HTWTP Long-Term Improvements	01-Jul-03 A	01-Dec-15
CUW36702 Peninsula Pipelines Seismic Upgrade	01-Jul-09 A	06-Jul-16
CUW36901 Capuchino Valve Lot Improvements (Com	22-Apr-05 A	19-Aug-08 A
CUW37101 Crystal Springs/San Andreas Transmission	18-Aug-03 A	23-Apr-14
CUW37801 Crystal Springs Pipeline No. 2 Replacemen	15-Jan-04 A	25-Sep-13
CUW37901 San Andreas Pipeline No. 3 Installation	15-Jan-04 A	21-Nov-11
CUW39101 Baden and San Pedro Valve Lots Improvem	03-Oct-05 A	01-Aug-12

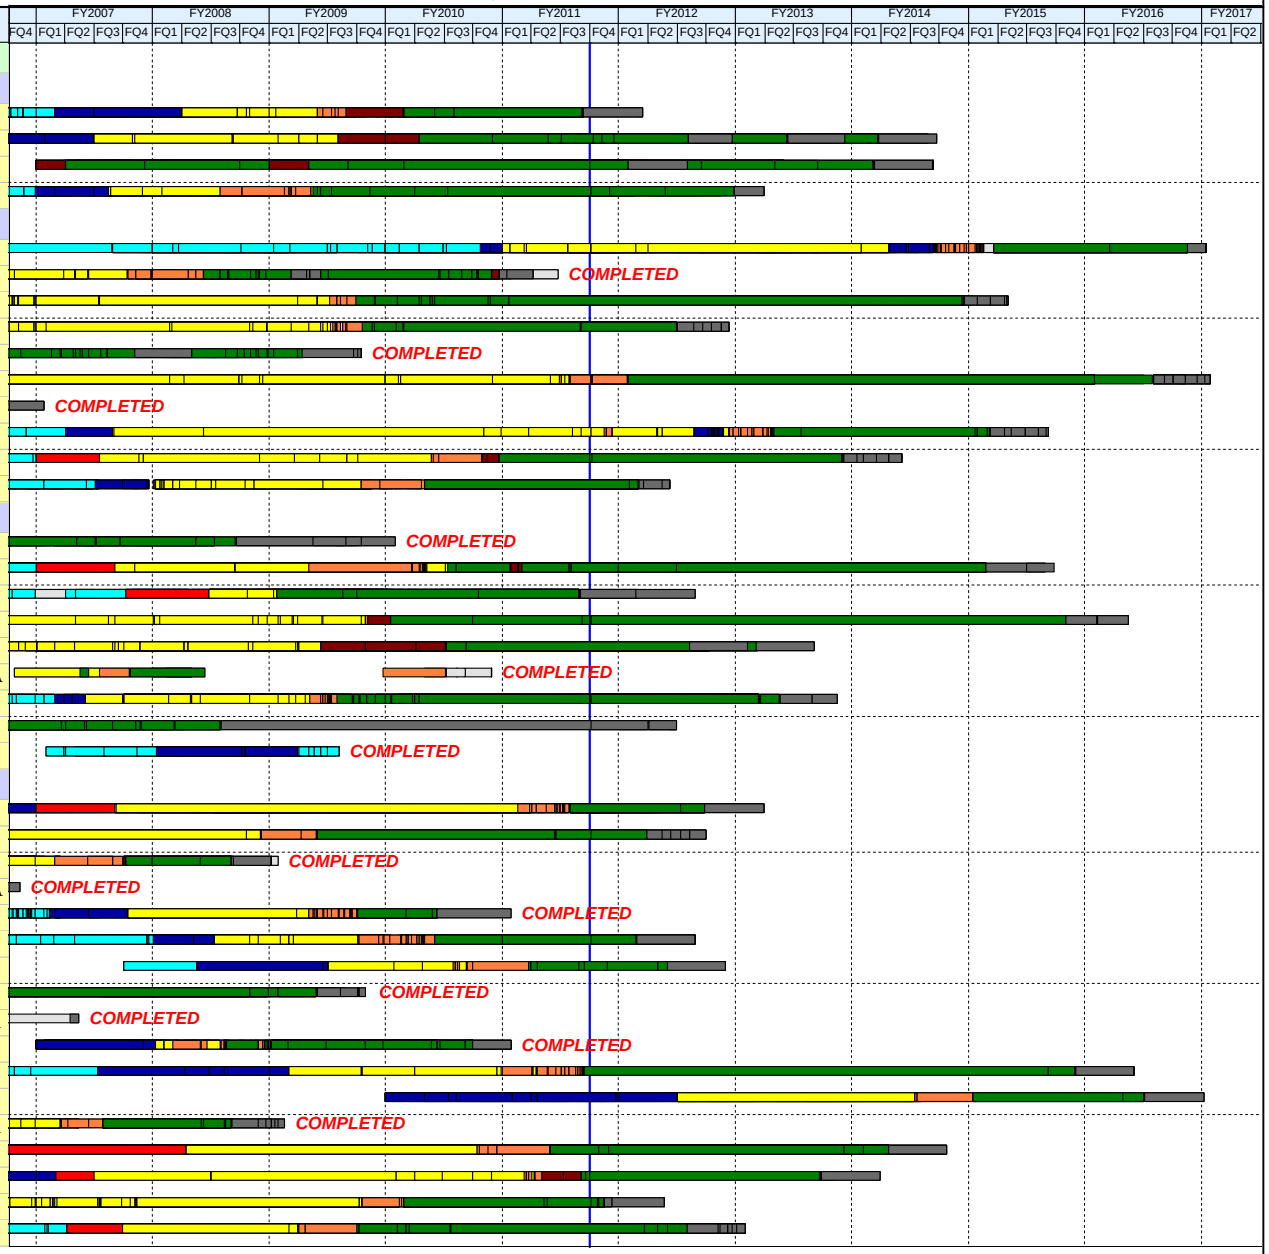

Project Management | Environmental | Right-of-Way | Construction Mgmt | Closeout
Planning | Design | Bid & Award | Construction | Program Mgmt

Revision Date: 06/10/11

ATTACHMENT 5: June 2011 Revised WSIP - Project-Level Schedules

Project Name	Start	Finish
San Francisco Regional Region	31-Mar-00 A	17-Jun-16
CUW30103 Regional Groundwater Storage and Recov	01-Jun-03 A	17-Jun-16
CUW35801 Sunset Reservoir - North Basin (Complete	31-Mar-00 A	10-Sep-10 A
CUW37201 University Mound Reservoir - North Basin	24-Oct-05 A	11-Jan-12
Support Projects	13-Apr-04 A	29-Jul-16
CUW36302 System Security Upgrades	07-Jan-06 A	29-Apr-16
CUW38801 Programmatic EIR (Completed)	13-Apr-04 A	30-Jun-09 A
CUW38802 Bioregional Habitat Restoration	06-Sep-06 A	24-Jun-16 A
CUW39201 Program Management Project	01-Aug-05 A	29-Jul-16
CUW39401 Watershed Environmental Improvement P	02-Jan-07 A	27-Jun-14

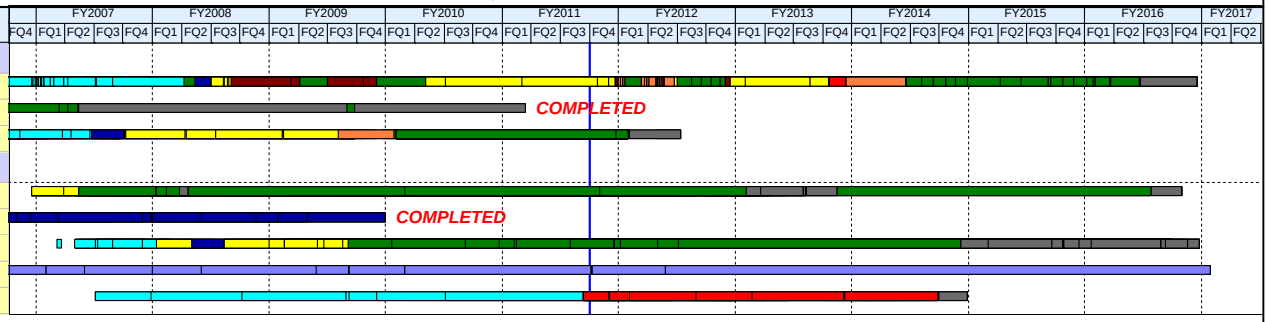

Project Management | Environmental | Right-of-Way | Construction Mgmt | Closeout
Planning | Design | Bid & Award | Construction | Program Mgmt

Revision Date: 06/10/11
